


NEW MCEWEN HIGH SCHOOL UPDATE

NEW 9-12 BUILDING UPDATES

- Exterior block wall construction in progress in Part C. Setting of second floor concrete planks complete. Planks being prepped for pouring concrete topping slab.
- Black waterproof membrane applied to exterior wall at outdoor seating area in Part A. Brick being set in front of insulation board, air gap, and tied into wall with brick ties.
- First coat of paint in progress throughout Part B.
- HVAC chase space walls constructed, and precast concrete planks set in place in Part C. Openings in walls and concrete planks in place for future running of HVAC ducts.
- Electrical conduit installation in progress throughout Part C on the underside of precast concrete planks.

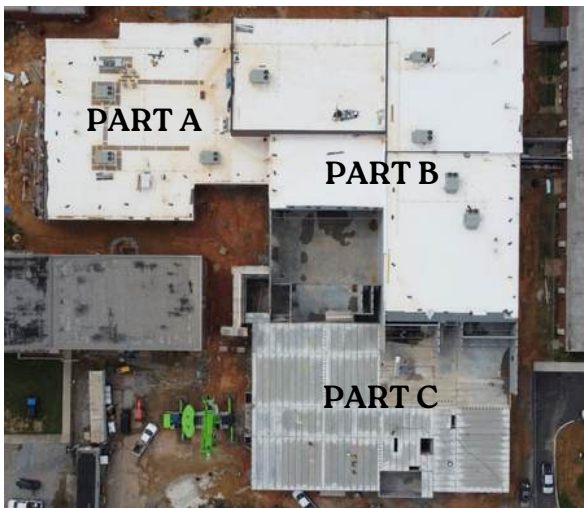

6-8 BUILDING ADDITION



- Caulking around exterior door frames complete.
- Final door hardware to be installed.
- Hand dryers installed in restrooms.
- Ceiling installed in the alcove where movable wall panels are stored.
- Movable wall panels to be installed.
